


Stadium Progress Update

School Board Meeting

March 10, 2022



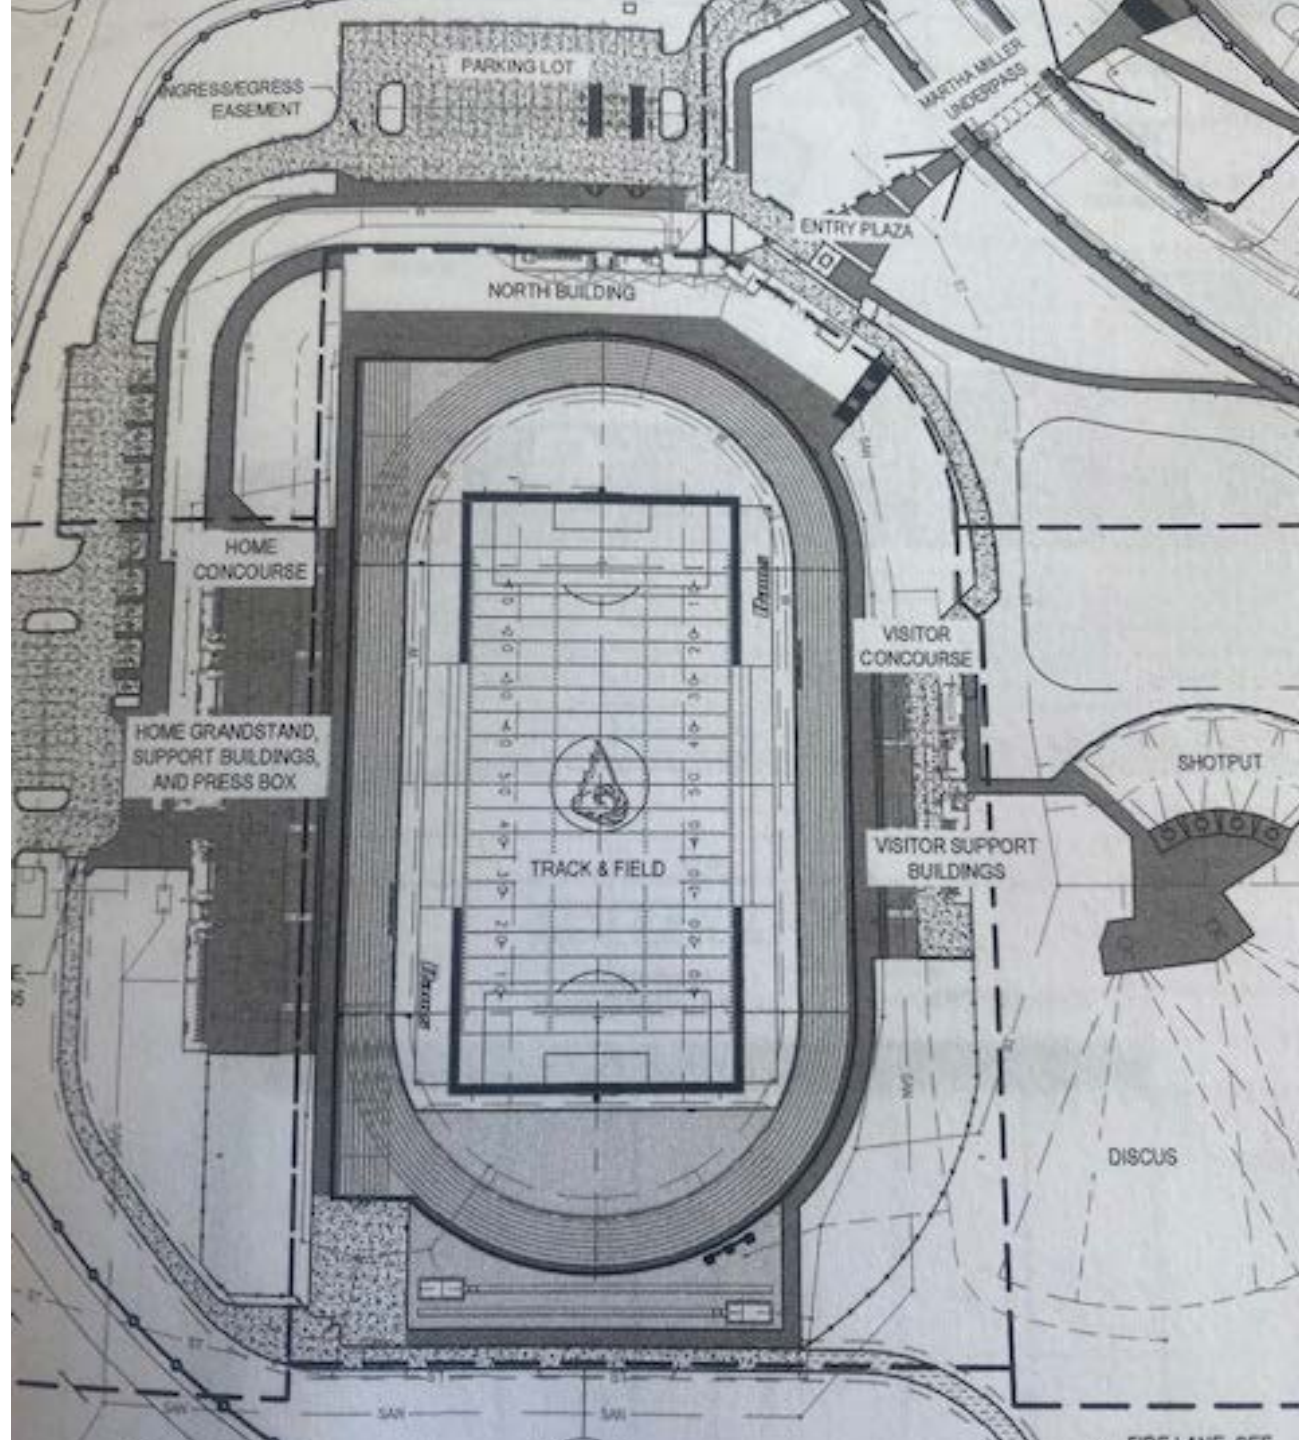




Retaining wall view from west to east



East side backfill behind retaining wall

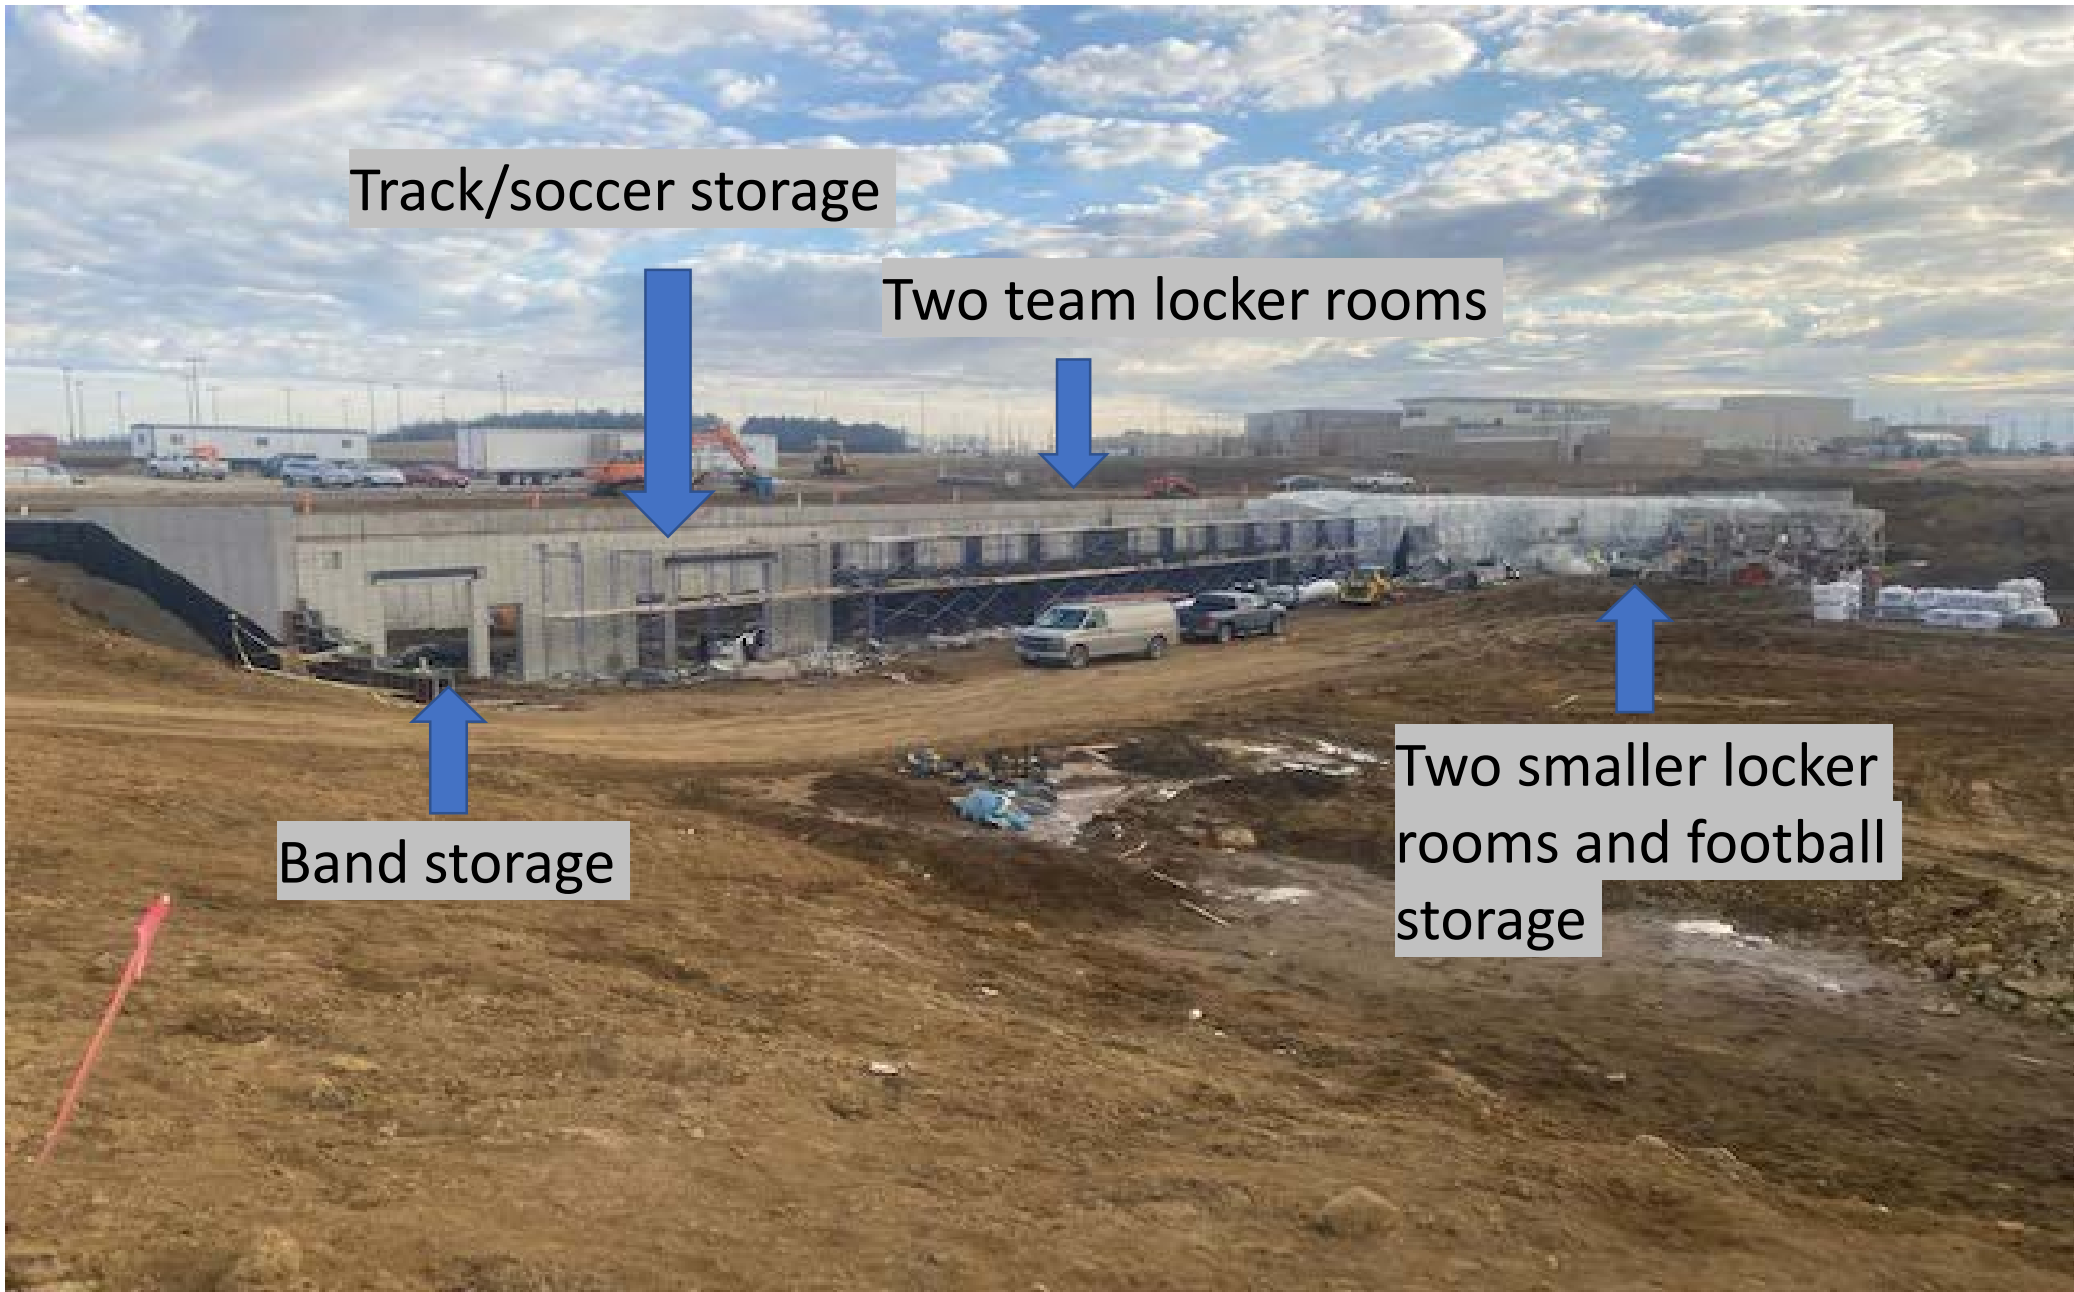

Track/soccer storage

Two team locker rooms

Band storage

Two smaller locker rooms and football storage

North building



Football storage


Two small locker rooms

NE portion of north building

Two team locker rooms



Track/soccer storage



Band storage





Bleacher footings on west side



Recent Progress

- 70% of masonry complete in north lobby area.
- Electrical and plumbing rough-ins for north building underway.
- Dirt backfill behind east and west retaining walls (though slow because of frost).
- Supply chain status: Contractor has been very proactive in the timely delivery of materials. Upcoming material needs are either on site or in a warehouse awaiting need.
- 38% work complete including materials stored.



Upcoming work

- Martha Miller drive is scheduled to be closed April 19 – August 12. District working on communication plan for students and parents.
- Site utilities start again once frost is out of the ground (currently 1.5 to 3 feet of frost).
- Backfilling east and west retaining walls.
- Bleacher footings.
- Continued work on north building



Schedule

- Have been some “spirited” meetings with contractors as a result of scheduling priorities. Have resulted in some improvements to schedule.
- Weather the next month will be a key to progress. Considerable site work can be accomplished once frost gone and available dry days.
- Schedule discussions happen every week.
- Current schedule shows October 2022 completion.



As project becomes more “vertical”, excitement is growing for vision of what a great facility this will be for students.

